

Distribution Transformer Quotation Summary

Howard Industries, Inc. Laurel, MS 1 (601) 425-3151

Customer Name: WAYNE-SANDERSON

Date: 8/7/2023

Quote #: HR-2291-001

Transformer(s) will be built according to the specifications listed below.

Specification: Quoted per specification received with inquiry

Item: 3 Phase Pad Mount

Quantity: 2

Type of Pricing: Order

Standard: IEEE Standard

UL Listing: UL Labeled

KVA: 2500

Primary Voltage: 12470 Grd Y / 7200 95 kV BIL

Live / Dead: Dead Front

Feed: Loop Feed

Taps: Taps Split - 2 2½% Above and Below

Primary Bushing: 200 Amp Bushing Wells with Standard Inserts and Replaceable Studs

Secondary Voltage: 480 Y / 277 30 kV BIL

Secondary Bushing: 10 Hole Spade with Supports

Fluid Type: Mineral Oil

Winding Conductor: HI Standard

Cooling: ONAN (OA) - Self Cooling

Temp Rise: 65 Degree C

Frequency: 60 HZ

Nominal Impedance: Minimum 5.3

Altitude: Less than 1000 m(3300ft)

Sound Level: NEMA Standard

Paint: Padmount Green - Munsell Green #7.0GY-3.29/1.5

Gauges: Thermometer

Gauges: Liquid Level

Gauges: Pressure Vacuum

Valves: Standard PRV

Valves: 1" Drain Valve with Sampler

Valves: Schrader Valve

Valves: Top Filler Valve

Valves: Nitrogen Port / Test Point

Switches: 1 - 2 Position

Switches: 300 Amp

Fusing: High Amp Bay-O-Net in Series with CLF (DUAL)

Spare Fuses: None

Primary Arresters: Elbow



Primary Arresters:Quantity 3
Primary Arresters:10 kV
K Rating:Howard Industries Standard
Tank Material:Mild Steel
Insulators /
Bushings: No Insulators / Bushings
Protective Caps:No Protective Caps
Dead End Well
Plugs: No Well Plugs
Customer Notes:

Providing Transformer Only

Unit Price:
Quantity:
Total Price:

Please review the features listed above to insure compliance with your specification or/and application.

DESCRIPTION	
1	LV BUSHING W/INT. 10H SPADE
2	LV SPADE SUPPORT
3	2 HOLE HORIZ NEMA GRD PAD
4	HV LB INSERT UNIV 95 BIL 200A
5	LOADBREAK PARKING STAND
7	NP ON DOOR, SERIAL ON TANK
8	TANK
9	COOLING RADIATORS
10	HANDHOLE & SECURITY COVER
12	LIFTING LUGS
13	JACKING PROVISIONS
14	2 HOLE HORIZ NEMA GRD PAD
15	1 IN DRAIN VALVE AND SAMPLER
21	PADLOCKABLE DOOR HANDLE
22	3 PT LATCH PENTA SEC BOLT
24	18 IN REMOVABLE SILL
25	METAL LV-HV BARRIER
39	CLIP ON DRIP SHIELD
41	BAYONET FUSE HOLDER
43	2 POSITION LOADBREAK SWITCH
47	PRV VAT 301-010-01N
48	DIAL THERM W/MAX POINTER
49	2" MAGNETIC LL GAUGE
50	OIL LEVEL PLUG
51	TAP CHANGER HANDLE
57	PRES VAC GAUGE
61	SCHRAEDER PENTADN 200A
A	BAY-O-NET FUSE
B	CURRENT LIMITING FUSE (DUAL)
C	
D	
E	
CAT NO	9196152291001
DWG BY TW	DATE: 08/04/23
APP BY	CC. 745

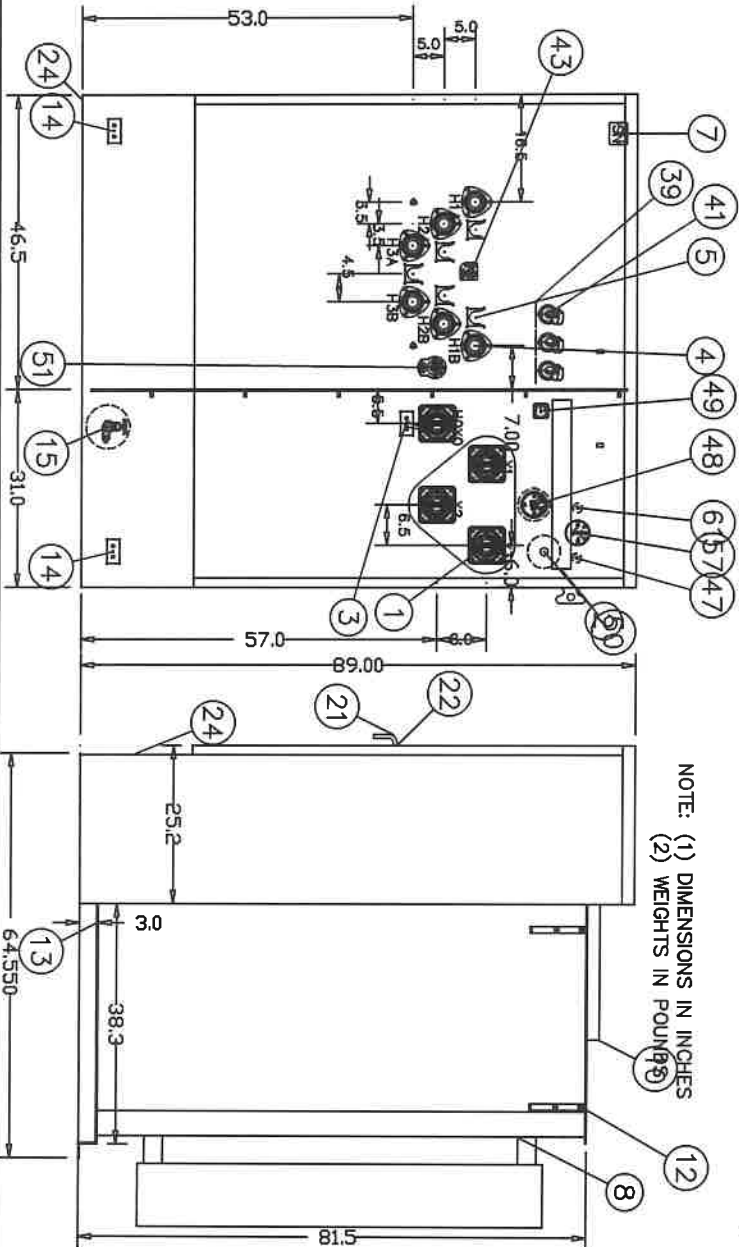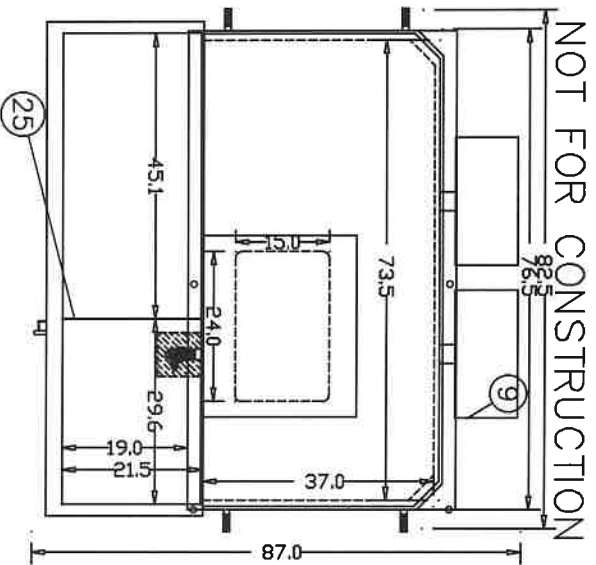

NOTE: THE WEIGHTS AND DIMENSIONS ARE APPROXIMATE AND SUBJECT TO CHANGE WITHIN THE CUSTOMER SPECIFIED LIMITS. APPROVAL DRAWINGS WITH THE ACTUAL WEIGHTS AND DIMENSIONS WILL BE PROVIDED UPON REQUEST AFTER RECEIPT OF ORDER.

DWG NO.	HR2291001
HOWARD INDUSTRIES INC.	
LAUREL, MISS. USA 39440	
THREE PHASE PAD DISTRIBUTION TRANSFORMERS	
CUSTOMER : QUOTES	
SPEC. H.I. STD.	DATED
KVA 2500.0BIL 95 TAPS TS-2 ABOVE 2 BELOW	
HIGH VOLTAGE 12470GRDY/7200	
LOW VOLTAGE 480Y/277	
APPROX. CORE AND COIL WEIGHT	10625
APPROX. TANK AND ACCESS. WEIGHT	2592
GAL. OF OIL 649, APPROX. WEIGHT	4868
APPROX. TOTAL WEIGHT	18085
REV. DATE DESCRIPTION BY APP	
A	

HR2291001

HR2291001

THREE PHASE
TRANSFORMER
DOE COMPLIANT

HOWARD INDUSTRIES



LAUREL MS 39440 USA

READ INSTRUCTION HI 105 BEFORE OPERATING MFG

KVA 2500

BIL	HV	95 LV	30 kV	%MP

HV 12470GRDY/7200


LV480Y/277 AMPS 3005

WT	TANK	c&c	TYPE
LB	2592	1062	OIL

4868 LBS TOTAL 18085 LBS
649 GAL

CONT 65 °C RISE CLASS ONAN 60HZ
TANK DESIGNED FOR +7 PSIG
F1 CLF PARTIAL RANGE
F2 BAYONET FUSE

CONTAINS NO DETECTABLE LEVEL OF PCP (LESS THAN 2 PPM) AT THE TIME OF MANUFACTURE

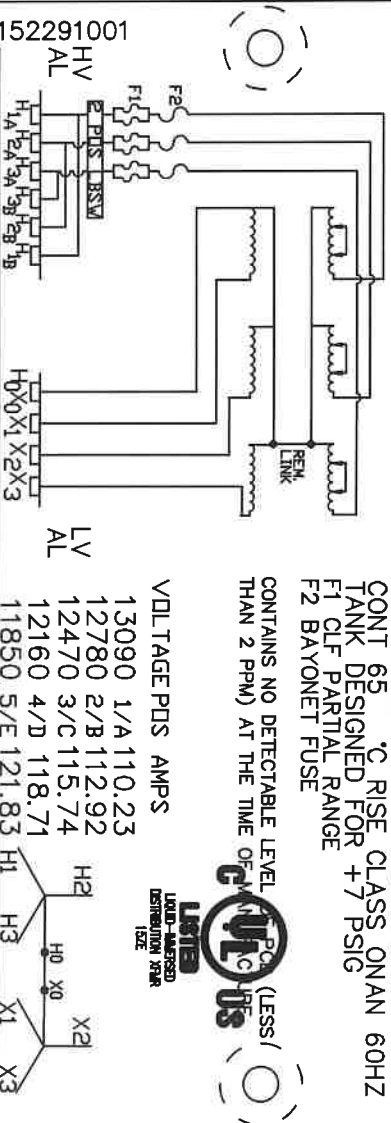

9196152291001

SER. NO.

SER. NO. BAR CODE

CAT. NO. BAR CODE

[illegible]

Howard Industries, Inc. Distribution Transformer Division

P.O. Box 1588 / Laurel, MS 39441-1588 / Voice: (601) 425-3151 / Fax: (601) 649-8090
E-mail: mkt@howard-ind.com

ALL ORDERS/CHANGE ORDERS THAT HAVE NOT BEEN PREVIOUSLY DESIGNED WILL REQUIRE APPROVAL DRAWINGS WHICH WILL BE AVAILABLE IN 30-40 BUSINESS DAYS AFTER ACCEPTANCE OF ORDER/CHANGE ORDER. ORDERS/CHANGE ORDERS WILL BE RELEASED FOR PRODUCTION SCHEDULING WITHIN 3 DAYS AFTER SIGNED APPROVAL DRAWINGS HAVE BEEN RECEIVED AT THE FACTORY. LEADTIMES BELOW ARE SUBJECT TO FACTORY LOADING AT TIME OF DRAWING RELEASE AND/OR MATERIAL AVAILABILITY.

LEADTIME

Product Description	Lead-time (wks after Release of Order/Change Order)
Poles (5kVA and below)	100
Poles (10kVA and above)	100
Single Phase Padmounted up to 250kVA	100
Three Phase Padmounted (500kVA and below)	54
Three Phase Padmounted (750kVA – 2500kVA)	54
Three Phase Padmounted (2501kVA-3750kVA)	54
Substations (225kVA-3750kVA)	54
Substations & Padmounts (3751kVA-10000kVA)	54
Three Phase Poles	100
Regulators	32
Junction Boxes/Switchpads	100

ADDITIONAL TIME REQUIRED ON TRANSFORMERS WITH THESE FEATURES:

****Transformers containing Stainless Steel may be delayed approximately 12 weeks****

1. Any test other than production line test – 1 week
2. Non standard, High Accuracy CT's – 1 week
3. Special Impedance – 1 week
4. Stack Core (On transformers less than 5000kVA) – 4 weeks
5. Dual Voltage with Taps – 2 weeks
6. Tri Voltage – 2 weeks
7. 200kV BIL – 4 weeks
8. 250kV BIL – 8 weeks
9. Secondary voltage above 600v – 2 weeks
10. Live Front Fusing – 2 weeks
11. Seismic requirement – At additional cost unless specified on quotation and based on specification requirements.
12. Retrofit – 2 weeks
13. Digital kWH meters – 2 weeks
14. Class 1 Division II – 2 weeks
15. NGR – 2 weeks
16. Special Sound Level – 2 weeks
17. Other special tests or items not on the configurator – minimum 2 weeks or more
18. Special paint colors – no additional time required if chip received within one week of order, otherwise – 2 weeks
19. Medium voltage Interrupter – 8 weeks

NOTE: 1) Additional time required is not cumulative
